

HOME INSPECTION REPORT


Inspector: Patricia Nguyen, ASHI #189234
Property: 456 Test Ave, San Jose CA 95123
Date: June 13, 2026

ROOF SECTION

Condition: DEFICIENT

Composition shingle roof, approximately 25 years old.
Multiple areas of curling and missing shingles observed.

Photo 1: Water stain on master bedroom ceiling



Brownish water stain ~2ft diameter

FOUNDATION SECTION


Condition: MARGINAL

Concrete perimeter foundation with slab-on-grade.

Hairline crack on east wall, approximately 3 feet long.

No vertical displacement. Monitor recommended.

Photo 2: Foundation crack, east wall exterior

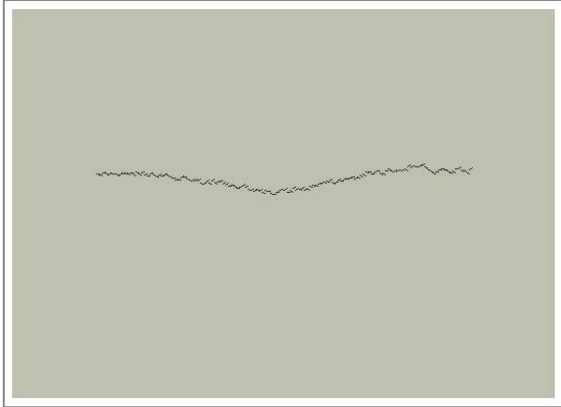

Hairline crack running horizontally

ELECTRICAL SECTION

Condition: SATISFACTORY

200 amp panel. All circuits labeled.

Two outlets in garage tested open ground.

Recommend repair (\$150-\$250).
